

**KARAYOLLARI GENEL MÜDÜRLÜĞÜ**  
**BÖLÜNmüş YOL VE TEK YOL ÇALIŞMALARI**

BÖLÜNmüş YOLLAR		TOPLAM (km)	
2002 SONU		6.101	
2003		1.362	
2004		1.791	
2005		2.050	
2006		1.481	
2007		1.082	
2008		1.492	
2009		2.117	
2010		2.227	
2011		1.525	
2003-2011 TOPLAMI		15.126	
GENEL TOPLAM	BSK	9.305	21.227
	SK	11.922	

TEK YOLLAR	TOPLAM (km)
2003	582
2004	757
2005	240
2006	459
2007	496
2008	548
2009	809
2010	1167
2011	1118
TOPLAM	6176

## KARAYOLLARI GENEL MÜDÜRLÜĞÜ BÖLÜNMÜŞ YOL ÇALIŞMALARI ÖNEMLİ AKSLAR

AKS ADI	BÖLÜNMÜŞ YOL PROJE UZUNLUĞU	2002 SONU		2003-2010 ARASI				31.12.2011 TARİHİNE KADAR YAPILAN BÖLÜNMÜŞ YOL ÇALIŞMALARINDAKİ MEVCUT DURUM (2011 YILINDA)								KALAN	TOPLAM TRAFİĞE AÇILAN YOL		
		BSK	SK	BSK		SK		TOPRAK İŞLERİ SEVİYESİNDE		ÜST YAPI SEVİYESİNDE		BSK		SK			BSK	SK	
				KGM	VALİLİK	KGM	VALİLİK	KGM	VALİLİK	KGM	VALİLİK	KGM	VALİLİK	KGM	VALİLİK				
ANKARA-SAMSUN YOLU	392,5	158,1		234,4													392,5		
		128,3	29,8	215,8		18,6										0,0	344,1	48,4	
ANKARA – AFYON – İZMİR YOLU	562,0	262,4		299,6													562,0		
		262,4		244,6		55,0										0,0	507,0	55,0	
(ANKARA – AKSARAY) AYR.-KULU-KONYA YOLU	155,0	28,7		126,3													155,0		
		28,7		126,3														155,0	
ANKARA – AKSARAY – EREĞLİ AYR YOLU	302,0	27,6		274,4													302,0		
		12,6	15,0	81,6		192,8											94,2	207,8	
AFYON-SANDIKLI-BURDUR-ANTALYA YOLU	262,0	38,4		223,6													262,0		
		4,5	33,9	79,6		144,0											84,1	177,9	
BOZÜYÜK-MEKECE-ADAPAZARI YOLU	134,0			134,0													134,0		
				134,0													134,0		
ŞANLIURFA – HABUR YOLU	367,0	34,3		332,7													367,0		
		34,3		187,5	4,0	115,7	25,5										225,8	141,2	
GEREDE-MERZİFON-NİKSAR-REF-ERZİNCAN-ERZURUM-AĞRI-DOĞUBEYAZIT YOLU	1243,0	77,3		1016,0				13,7		120,8					1214,1				
		59,5	17,9	478,5	6,0	417,4	114,1	13,7			87,5		33,3	28,9	631,5	582,6			
SİVRİHİSAR-ESKİŞEHİR-BURSA YOLU	245,0	66,0		173,2													239,7		
		66,0		168,2		5,0					0,5			5,3	234,7	5,0			
BURSA-BALIKESİR-AKHİSAR-MANİSA-İZMİR YOLU	323,0	102,0		218,0													323,0		
		66,9	35,1	169,5		48,5					3,0			0,0	239,4	83,6			
KARADENİZ SAHİL YOLU	542,6	233,7		308,9													542,6		
		233,7		308,9													542,6		
ANKARA-ACYURT-ÇANKIRI-KASTAMONU YOLU	232,4	27,5		174,4				3,2		10,3					212,2				
		9,0	18,5	3,5	143,1	27,8	3,2				3,0	2,3	4,9	20,2	15,5	196,7			
AFYON-KONYA-EREĞLİ-(AKSARAY-POZANTI)AYR. YOLU	389,0	69,9		303,9													389,0		
		69,9		14,3		270,3	19,3					15,2		0,0	14,3	374,7			
BOZÜYÜK-KÜTAHYA-AFYON YOLU	152,0	0,3		149,0													152,0		
			0,3			149,0					1,4		1,3		1,4	150,6			
KINALI AYR. – TEKİRDAĞ – İPSALA YOLU	179,0			179,0													179,0		
				173,0		6,0									173,0	6,0			
KONYA-KARAMAN-MUT-SİLİFKE YOLU	249,0	35,2		140,4													193,7		
			35,2	12,0		94,1	34,3					18,1		55,3	12,0	181,7			
KAYSERİ- GÜRÜN-DARENDE-MALATYA YOLU	334,0	29,6		271,3				2,0		22,1					323,0				
		29,6		3,0		268,3		2,0				22,1		11,0	3,0	320,0			
MALATYA-ELAZIĞ-BİNGÖL-MUŞ-BİTLİS YOLU	422,0	64,0		343,5													422,0		
		6,0	58,0	42,7		262,6	38,2					14,5			48,7	373,3			
ELAZIĞ – DİYARBAKIR YOLU	149,0	14,0		104,0													129,0		
			14,0	9,0		95,0							11,0	20,0	9,0	120,0			
YILDIZELİ-TOKAT-AMASYA	182,1	5,4		148,5													162,3		
		4,1	1,4	47,3		101,2					8,2		0,2	19,8	59,6	102,8			
DİYARBAKIR – BATMAN YOLU	93,0	8,0		77,0													85,0		
			8,0	21,0		24,0	32,0							8,0	21,0	64,0			
KIRIKKALE-KIRŞEHİR-KAYSERİ YOLU	231,0	53,0		153,0													206,0		
			53,0	67,5		85,5								25,0	67,5	138,5			
(KIRIKKALE-DELİCE) AYR. – YOZGAT-SİVAS-REFAHİYE YOLU	486,0	21,2		464,8													486,0		
		3,8	17,4	150,5	8,5	299,8	6,0								162,8	323,2			
MERSİN-ERDEMLİ-SİLİFKE-ANTALYA	437,7	152,7		157,8													342,0		
		107,2	45,5	47,8		110,0							22,0	9,5	95,7	155,0	187,0		


31/12/2011

# BÖLÜNMÜŞ YOLLAR + DEVLET VE İL YOLLARI ÇALIŞMA TABLOSU (2011 YILI ARALIK AYI PROGRAM VE YAPILAN )

BÖLGE	BSK			K			K0			K1			TOPLAM		
	PROG.	YAPIL.	%	PROG.	YAPIL.	%	PROG.	YAPIL.	%	PROG.	YAPIL.	%	PROG.	YAPIL.	%
01.BÖLGE	210	497	236	207	334	161	116	35	30	10	18	180	543	884	163
02.BÖLGE	250	637	255	1,330	1,040	78	370	384	104	0	0	0	1,950	2,062	106
03.BÖLGE	263	525	200	1,167	1,202	103	333	424	127	0	0	0	1,763	2,151	122
04.BÖLGE	229	242	106	715	556	78	260	158	61	41	44	109	1,245	1,001	80
05.BÖLGE	71	162	227	1,148	961	84	217	382	176	0	0	0	1,436	1,504	105
06.BÖLGE	222	96	43	1,190	1,064	89	216	364	169	0	0	0	1,628	1,524	94
07.BÖLGE	58	314	541	800	622	78	280	222	79	20	6	30	1,158	1,164	101
08.BÖLGE	64	92	147	979	305	31	283	319	113	0	0	0	1,326	716	54
09.BÖLGE	216	222	103	890	1,077	121	125	163	130	10	7	70	1,241	1,468	118
10.BÖLGE	193	53	27	517	376	73	164	56	34	127	51	41	1,001	536	54
11.BÖLGE	66	121	183	688	872	127	302	551	182	40	26	66	1,096	1,569	143
12.BÖLGE	83	98	118	1106	586	53	423	212	50	15	6	40	1,627	901	55
13.BÖLGE	117	90	77	698	571	82	352	370	105	0	4	0	1,167	1,035	89
14.BÖLGE	118	154	130	760	778	102	252	257	102	0	0	0	1,130	1,188	105
15.BÖLGE	133	143	107	795	1,071	135	195	244	125	0	20	0	1,123	1,478	132
16.BÖLGE	164	231	141	430	644	150	432	320	74	78	26	34	1,198	1,222	111
<b>TOPLAM</b>	2,458	3,675	150%	13,420	12,059	90%	4,320	4,461	103%	341	209	%61	20,538	20,404	99%

ASTARLI SATHİ KAPLAMA YAPIMI (K1)	201	Km.
ASTARLI SATHİ KAPLAMA ONARIMI (K0)	4461	Km.
ASTARSIZ SATHİ KAPLAMA ONARIMI (K)	12059	Km.
BSK YAPIMI (BSK)	3675	Km.
<b>GENEL TOPLAM</b>	<b>20404</b>	<b>km.</b>

**BİTÜMLÜ SICAK KARIŞIM KAPLAMA YAPIM VE ONARIM  
GERÇEKLEŞMELERİ  
(2011 YILI ARALIK AYI)**

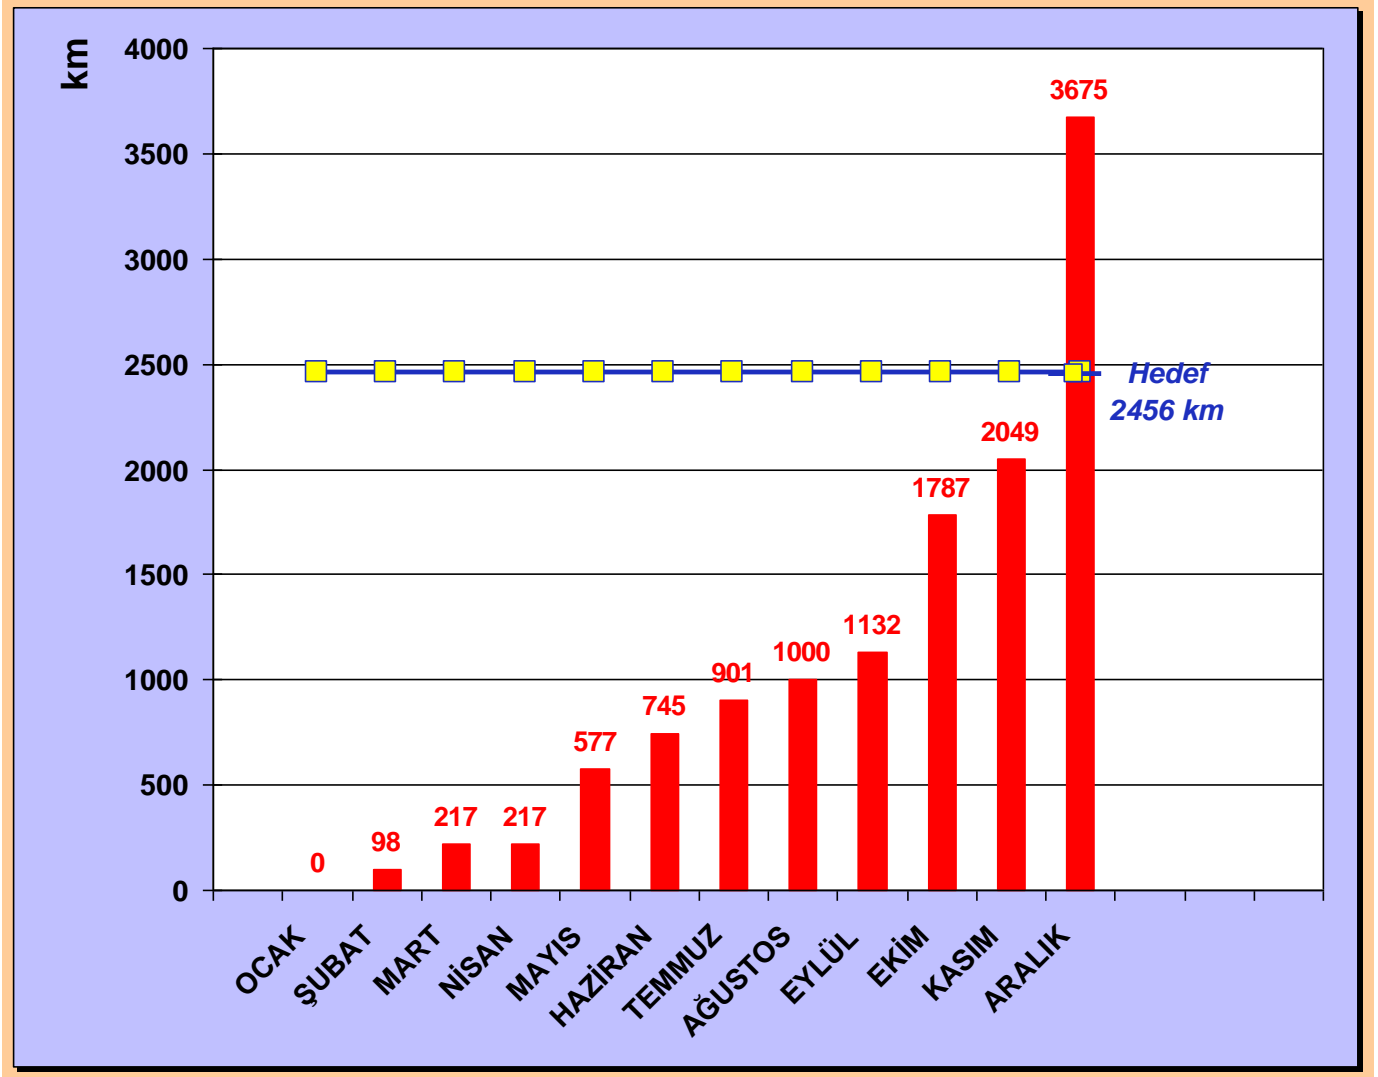

**SATHİ KAPLAMA YAPIM VE ONARIM  
GERÇEKLEŞMELERİ  
(2011 YILI ARALIK AYI)**

